



# LIBRARY RENOVATION

Randy Culver | Associate VP, Facilities & Sustainability

— BLACK HILLS STATE UNIVERSITY —





# UPPER LEVEL ADDITION

- Concrete Pour and Precast









# UPPER LEVEL ADDITION

- Floor on Addition and “Building Your Future” Sign

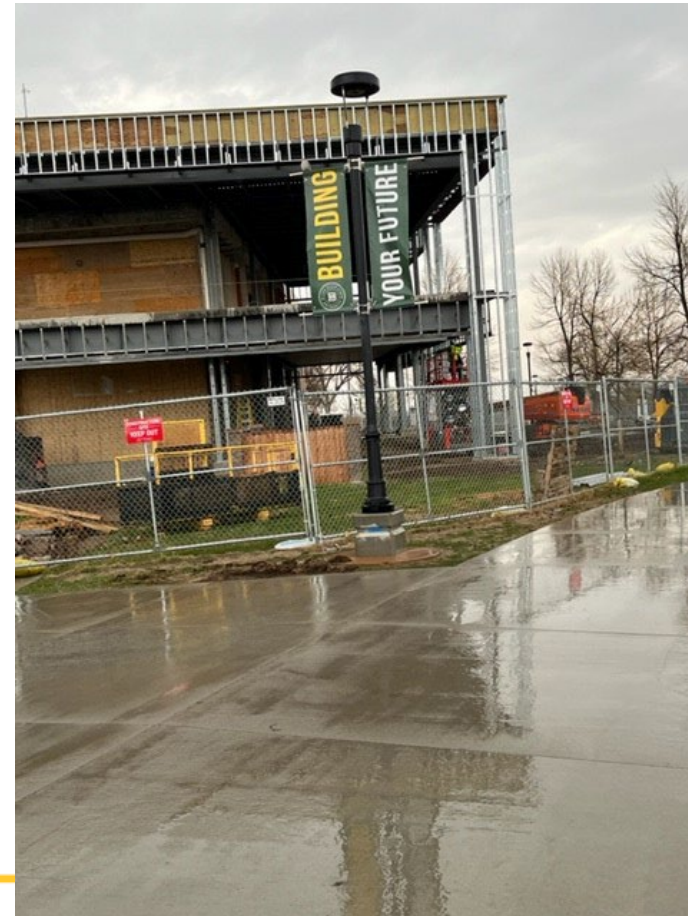



# LIBRARY RENOVATION TIMELINE

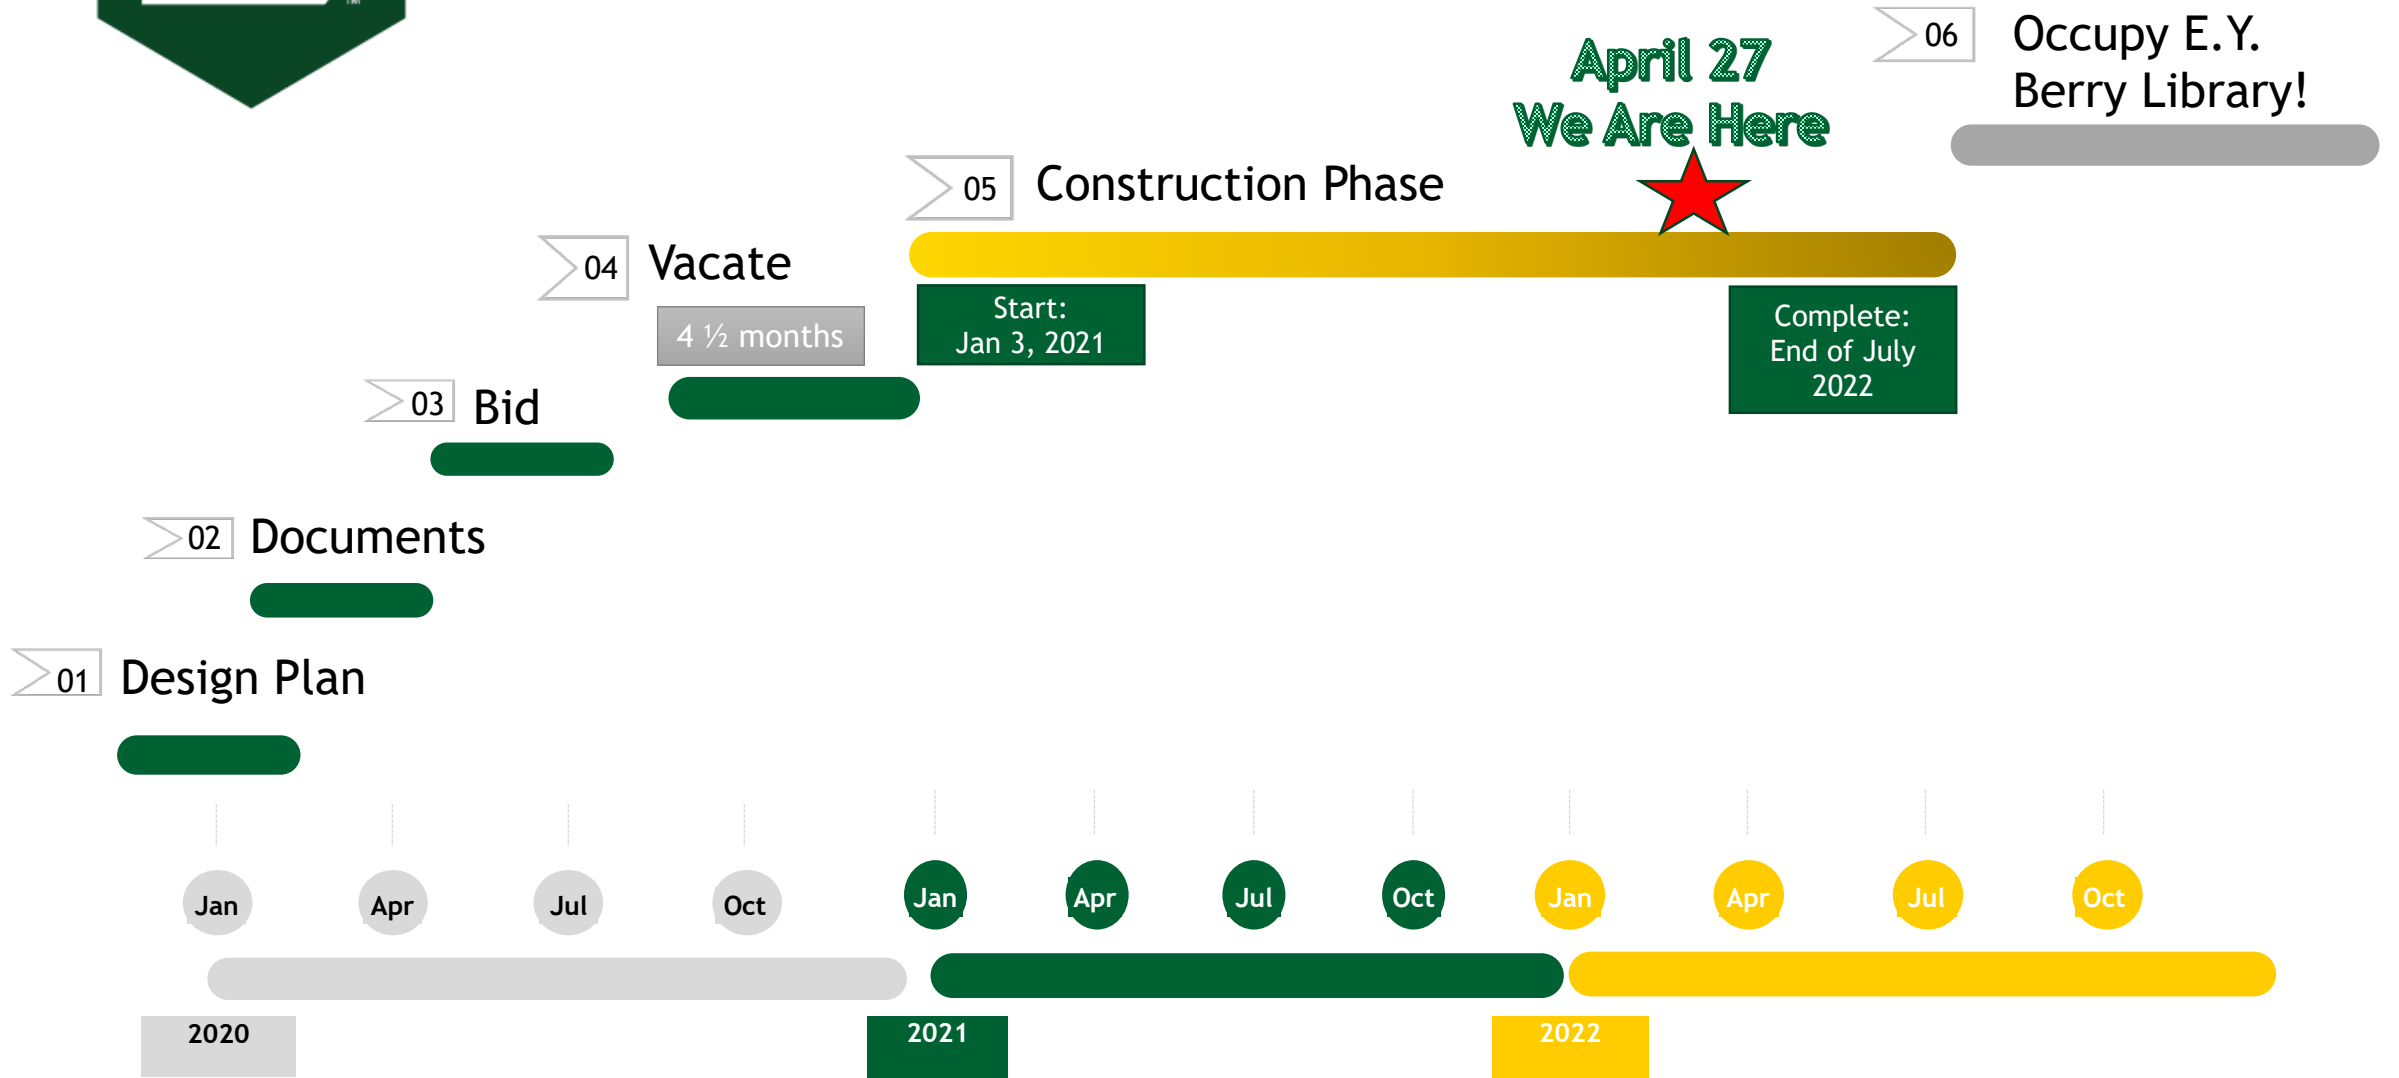



# PROJECT DELAYS DUE TO SUPPLY CHAIN

- Steel for upper level addition
  - Found a new vendor for steel
  - Could not find primer paint to paint iron
  - Kept project moving forward - worked interior items
- Short delay for glass for windows - nothing critical
- LED lighting delays - shortage of aluminum
  - LED lighting has been delivered
- Riss Cabinets and Casework Fire - 2 weeks ago!
  - Good news: 75% casework was already on BHSU site
  - Approx. 25% lost - café benches, shelves, nothing critical



# MOVE-IN PLAN / SCHEDULE

- Substantial construction completion - expected end of July 2022
- New furniture delivery/installed early August to mid-August
  - 3 Vendors will take 3 weeks to assemble and install
- Occupants and office furniture move-in early August through October
  - Focus on student service functions
  - Move furniture from storage
- Relocate Einstein's from Student Union
  - New counter tops being manufactured
- Move Book Collection and Archives in October- December
- Possible Library opening for limited use at start of Fall semester - August 22
- Thank you all for your patience!





# TOURS ON FRIDAYS

- Contact Mike Overby or Debbie Liddick to schedule
- Meet at Facilities Services to be equipped with safety gear
- Tour lasts approx. 1 hour

